ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
0		**UoW room booking system**	**35 days**	**Wed 1/4/20**	**Tue 19/5/2(**		
1		**1 Project Preparation phase**	**4 days**	**Wed 1/4/20**	**Mon 6/4/20**		
2		1.1 Interview users	2 days	Wed 1/4/20	Thu 2/4/20		Junior Tantono PM,Seri Da
3		1.2 Compile requirement	1 day	Fri 3/4/20	Fri 3/4/20	2	Junior Tantono PM,Neo Ka
4		1.3 Project Charter proposal and apporval	1 day	Mon 6/4/20	Mon 6/4/20	3	Junior Tantono PM
5		1.4 Completion of preparation phase	0 days	Mon 6/4/20	Mon 6/4/20	4	Junior Tantono PM
6		**2 Project Planning phase**	**10 days**	**Tue 7/4/20**	**Mon 20/4/2(**		
7		2.1 Scope statement	1 day	Tue 7/4/20	Tue 7/4/20	5	Junior Tantono PM,Neo Ka
8		2.2 Cost management plan	2 days	Wed 8/4/20	Thu 9/4/20	7	Junior Tantono PM,Neo Ka
9		2.3 Human resource Plan	2 days	Fri 10/4/20	Mon 13/4/20	8	Junior Tantono PM,Neo Ka
10		2.4 Project Scheduling	3 days	Tue 14/4/20	Thu 16/4/20	9	Junior Tantono PM,Neo Ka
11		2.5 Risk management plan	2 days	Fri 17/4/20	Mon 20/4/20	10	Junior Tantono PM,Neo Ka
12		2.6 Completion of project plannig phase	0 days	Mon 20/4/20	Mon 20/4/20	11	Junior Tantono PM
13		**3 Design Phase**	**15 days**	**Tue 21/4/20**	**Mon 11/5/2(**		
14		3.1 design UI	5 days	Tue 21/4/20	Mon 27/4/20	12	Decen Ng Programmer,Jin
15		3.2 Learning of PHP	5 days	Tue 28/4/20	Mon 4/5/20	14	Decen Ng Programmer,Jin
16		3.3 Design Database	5 days	Tue 5/5/20	Mon 11/5/20	15	Decen Ng Programmer,Jin
17		3.4 Completion of deisgn phase	0 days	Mon 11/5/20	Mon 11/5/20	16	Junior Tantono PM
18		**4 Testing phase**	**4 days**	**Tue 12/5/20**	**Fri 15/5/20**		
19		4.1 Test UI design	2 days	Tue 12/5/20	Wed 13/5/20	17	Decen Ng Programmer,Jin

Project: UoW room booking sy
Date: Sun 17/5/20



ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
20		4.2 Test Backend	2 days	Thu 14/5/20	Fri 15/5/20	19	Decen Ng Programmer,Jin
21		4.3 Completion of Testing phase	0 days	Fri 15/5/20	Fri 15/5/20	20	Junior Tantono PM
22		**5 Presentation Phase**	**2 days**	**Mon 18/5/2(**	**Tue 19/5/20**		
23		5.1 Prepare video for presentation	1 day	Mon 18/5/20	Mon 18/5/20	21	Decen Ng Programmer,Jing Jue
24		5.2 Rehearse for presentation	1 day	Tue 19/5/20	Tue 19/5/20	23	Decen Ng Programmer,Jing Jue
25		5.3 Completion of presentation phase	0 days	Tue 19/5/20	Tue 19/5/20	24	Junior Tantono PM
26		**6 Meeting**	**33 days**	**Wed 1/4/20**	**Mon 18/5/2(**		
27		6.1 Meeting minutes 1	0 days	Wed 1/4/20	Wed 1/4/20		Decen Ng Programmer,Jin
28		6.2 Meeting minutes 2	0 days	Mon 6/4/20	Mon 6/4/20		Decen Ng Programmer,Jin
29		6.3 Meeting minutes 3	0 days	Mon 13/4/20	Mon 13/4/20		Decen Ng Programmer,Jin
30		6.4 Meeting minutes 4	0 days	Thu 16/4/20	Thu 16/4/20		Decen Ng Programmer,Jin
31		6.5 Meeting minutes 5	0 days	Fri 24/4/20	Fri 24/4/20		Junior Tantono PM,Neo Ka
32		6.6 Meeting minutes 6	0 days	Fri 1/5/20	Fri 1/5/20		Decen Ng Programmer,Jin
33		6.7 Meeting minutes 7	0 days	Mon 18/5/20	Mon 18/5/20		Decen Ng Programmer,Jin
34		7 Completion of room booking system	0 days	Tue 19/5/20	Tue 19/5/20	25	Junior Tantono PM

Project: UoW room booking sy
Date: Sun 17/5/20



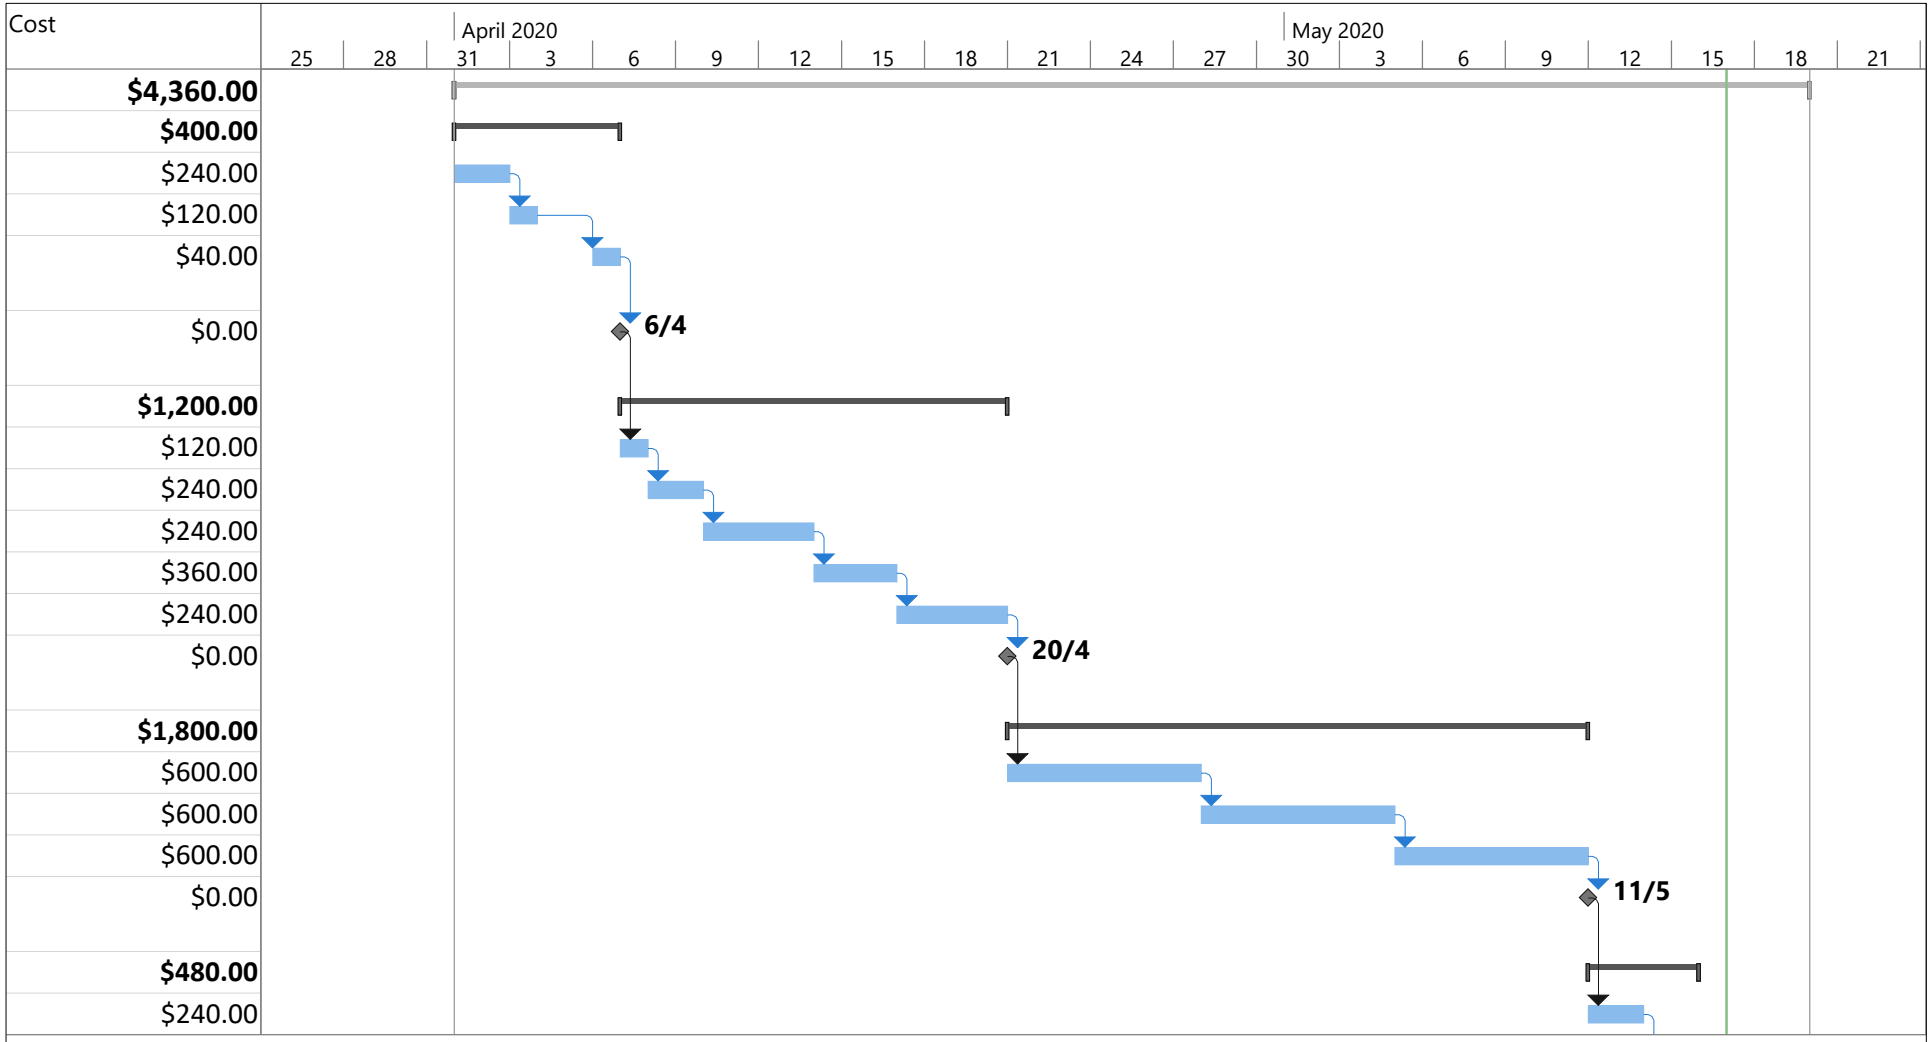

Project: UoW room booking sy
Date: Sun 17/5/20

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

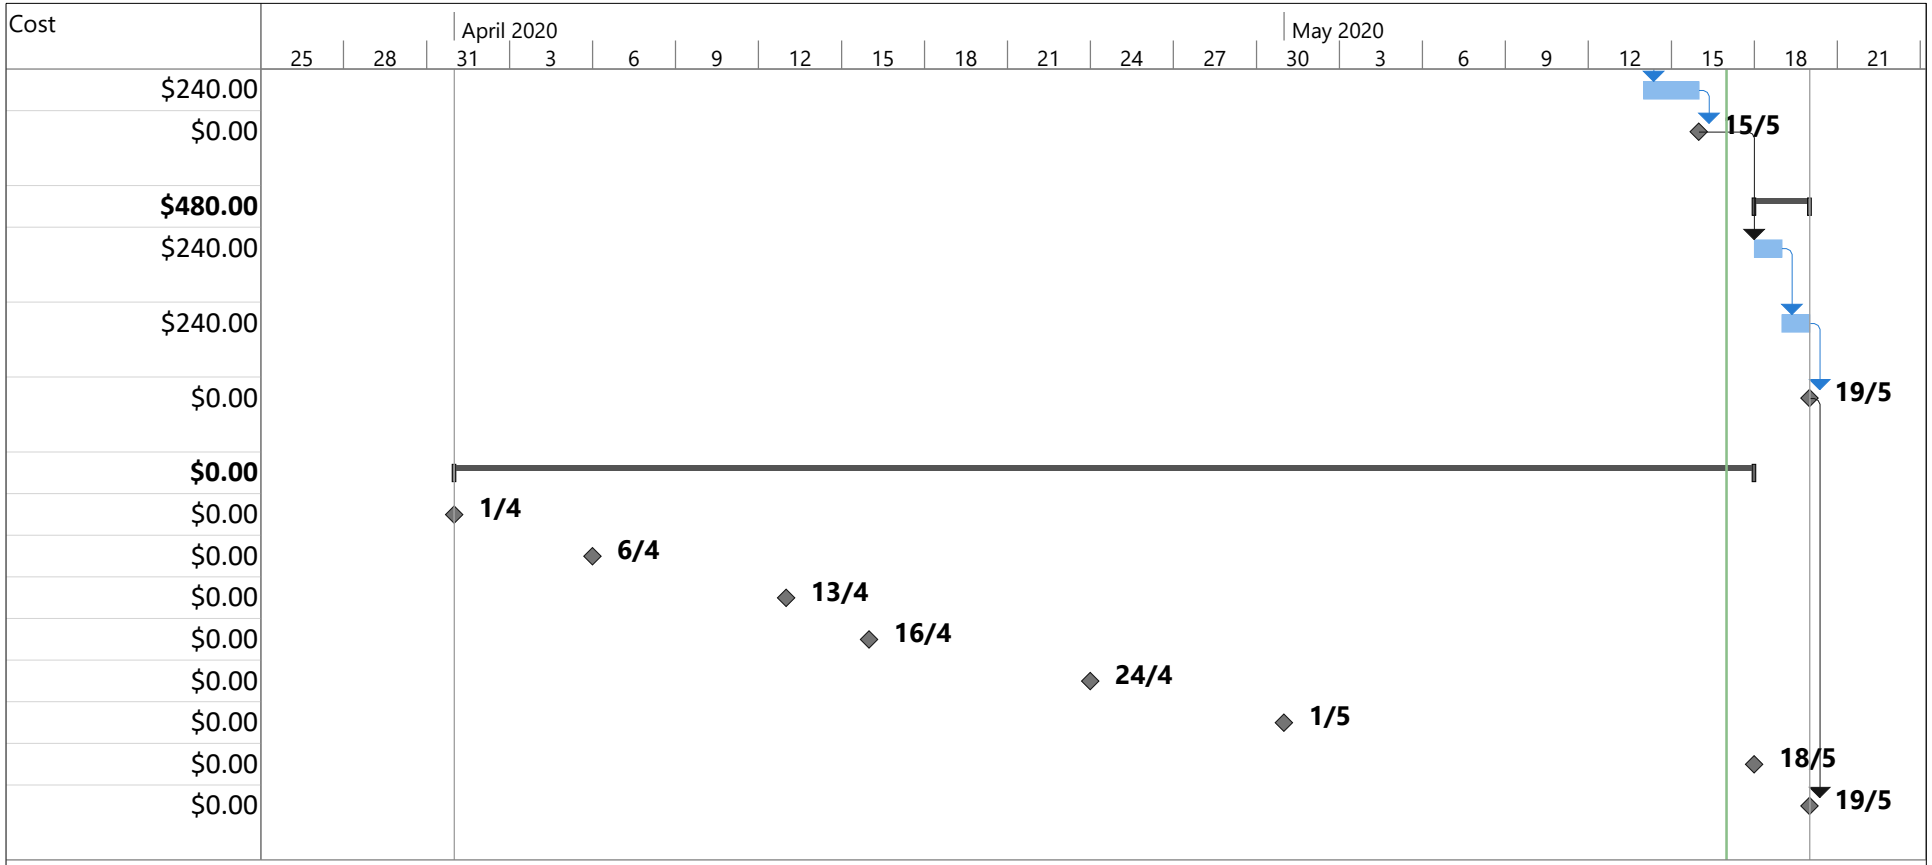

Project: UoW room booking sy
Date: Sun 17/5/20

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
